1. All bracing, blocking, beams, purlins @ 2'0" o.c., ledger, etc. provided by others.
2. Roof truss to roof truss connections provided by Riverside Roof Truss.
3. Truss to building connections provided by others.

Refer to Sealed drawings for connection detail of multiple ply trusses.

NOT ALL TRUSSES ARE SYMMETRICAL AND MAY NOT PERFORM CORRECTLY IF INSTALLED BACKWARDS. PLEASE REFER TO SEALS WHILE SETTING TRUSSES TO ENSURE TRUSSES ARE ORIENTED CORRECTLY



Products				
Net Qty	Plies	Product	Length	PlotID
3	1	11 7/8" NI-40x	44-00-00	FJ44
8	1	11 7/8" NI-40x	30-00-00	FJ30
4	1	11 7/8" NI-40x	26-00-00	FJ26
16	1	11 7/8" NI-40x	22-00-00	FJ22
3	1	11 7/8" NI-40x	18-00-00	FJ18
2	2	11 7/8" NI-40x	12-00-00	FJ12-2
2	2	11 7/8" NI-40x	8-00-00	FJ10-2
2	2	1 3/4" x 9 1/4" (2.0E 3100) LVL	38-00-00	BM8
2	2	1 3/4" x 9 1/4" (2.0E 3100) LVL	18-00-00	BM10
2	2	1 3/4" x 9 1/4" (2.0E 3100) LVL	18-00-00	BM9
15	1	1 1/8" x 11 7/8" APA Rim Board	12-00-00	RIM1
1	1	11 7/8" NI-40x	45-00-00	Bk1

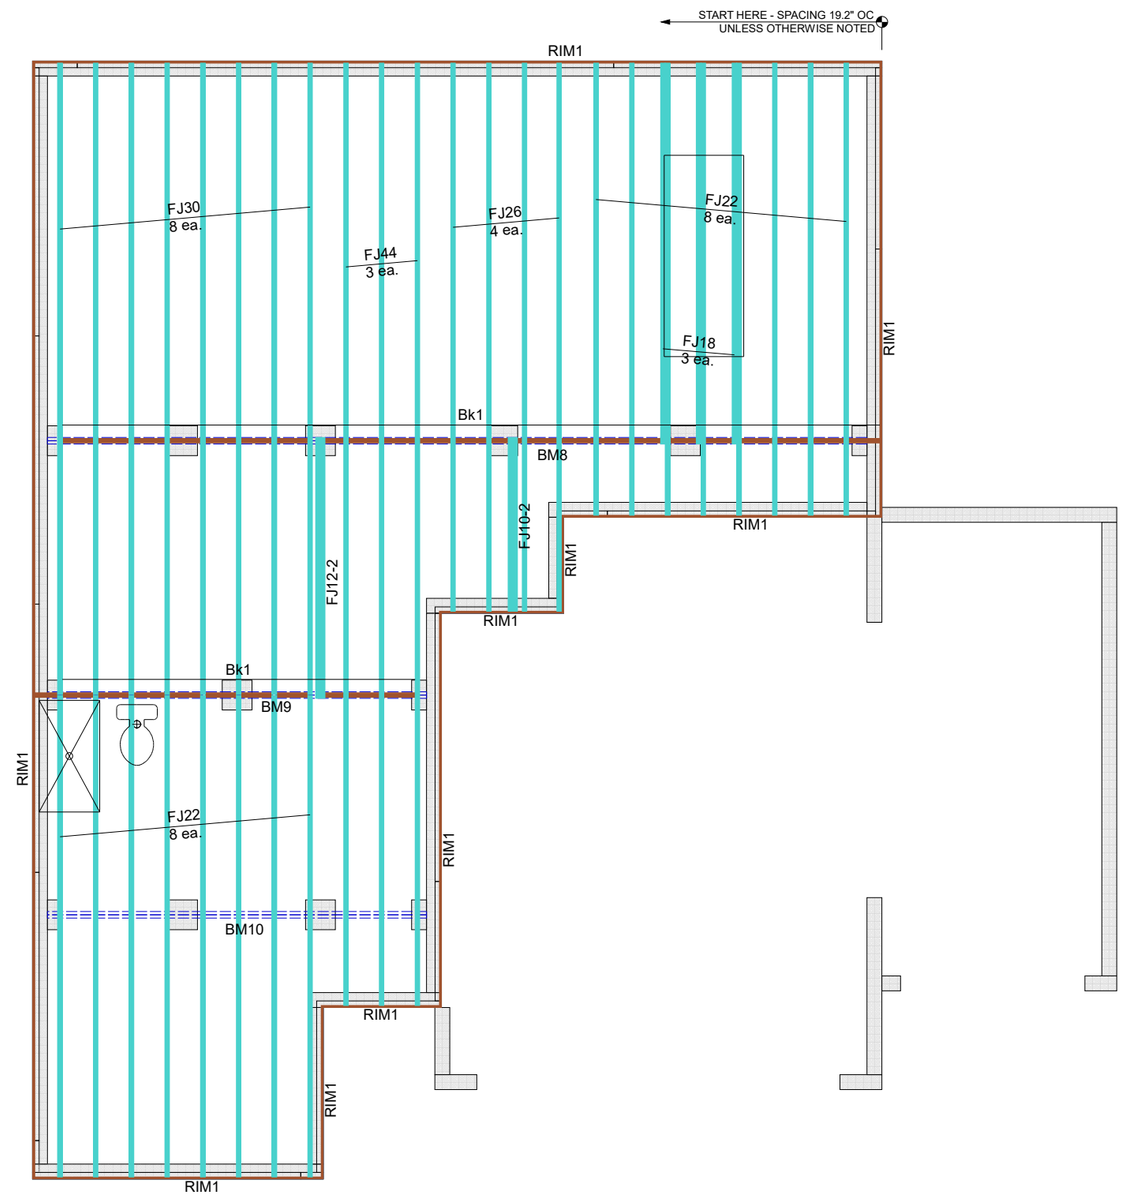

SHOP DRAWING APPROVAL
THIS LAYOUT IS THE SOLE SOURCE FOR FABRICATION OF TRUSSES AND VOIDS ALL PREVIOUS ARCHITECTURAL OR OTHER TRUSS LAYOUTS. REVIEW AND APPROVAL OF THIS LAYOUT MUST BE RECEIVED BEFORE ANY TRUSSES WILL BE BUILT. VERIFY ALL CONDITIONS TO INSURE AGAINST CHANGES THAT WILL RESULT IN EXTRA CHARGES TO YOU.

REVIEWED BY:_____ APPROVED BY:_____ DATE:_____

THIS IS A TRUSS PLACEMENT DIAGRAM ONLY. These trusses are designed as individual building components to be incorporated into the building design at the specification of the building designer. See individual design sheets for each truss design identified on the placement drawing. The building designer is responsible for temporary and permanent bracing of the roof and floor systems and for the overall structure. The design of the truss support structure including headers, beams, walls, columns, and sufficient blocking in floor capable of under point loads is the responsibility of the building designer. For general guidance regarding bracing, consult "Bracing of Wood Trusses" available from the Truss Plate Institute, 583 D'Onofrio Drive, Madison, WI 53179.

Client:	MATTAMY HOMES
Job Name:	SEQUOIA - FRENCH COUNTRY
Model:	EWP 1ST FLOOR
Lot #: 30	Subdivision:
Order #: 24-4363-B	Sales Rep: C Walden
Designer: R S	Date: 7/22/2024

Hanger Conversion Chart

USP	Simpson
JUS26	LUS26
THD26	HUS26
THD26-2	HHUS26-2
HJC26	THJA26
MSH422	THA422

733 RIVER PARK DRIVE
DANVILLE, VA 24540
(434) 793-0217
FAX: (434) 799-8767

RIVERSIDE ROOF TRUSS, LLC

Roof Surface Area: 0 Sq. Ft.
Floor Surface Area: 4288 Sq. Ft.

MiTek SIMPSON Strong-Tie
